



2019 Street Improvements Project Update

June 17, 2019

Please view the phasing map on page two.

Week of June 10

- Crews began installing storm sewer along 200th Street.
- Spot curb and sidewalk removal was completed for all phases of the project.

Week of June 17

- Storm sewer installation along 200th Street will be completed. Crews will then begin installing storm sewer on Chili and Chevelle Avenues.
- Spot curb and sidewalk will be poured on Monday, June 17th. Please refrain from driving on new curb for 7 days. If a piece of new curb/sidewalk is poured in front of your driveway please plan to park on the street in front of your home outside of working hours.
- The streets getting a partial reconstruct will be reclaimed later in the week/early the following week.

Parking, access, and detour information

During construction, the contractor will typically work from 7 a.m. to 7 p.m. On-street parking will not be available during working hours. If you need to leave past 7 a.m., you may need to park on another nearby street. Access to driveways will be restored at the end of each work day. If you have a recreational vehicle that you need a place to park during the concrete work the Township has approved parking in the Town Hall Parking Lot off of 197th Street.

Contacts

If you have any questions or concerns, please contact **Eric Hauser at (507) 276-6695.**




Be sure to sign up for email updates on the project website!

<http://clients.bolton-menk.com/empiretownship/2019-street-improvements-overview/>



Phasing Map

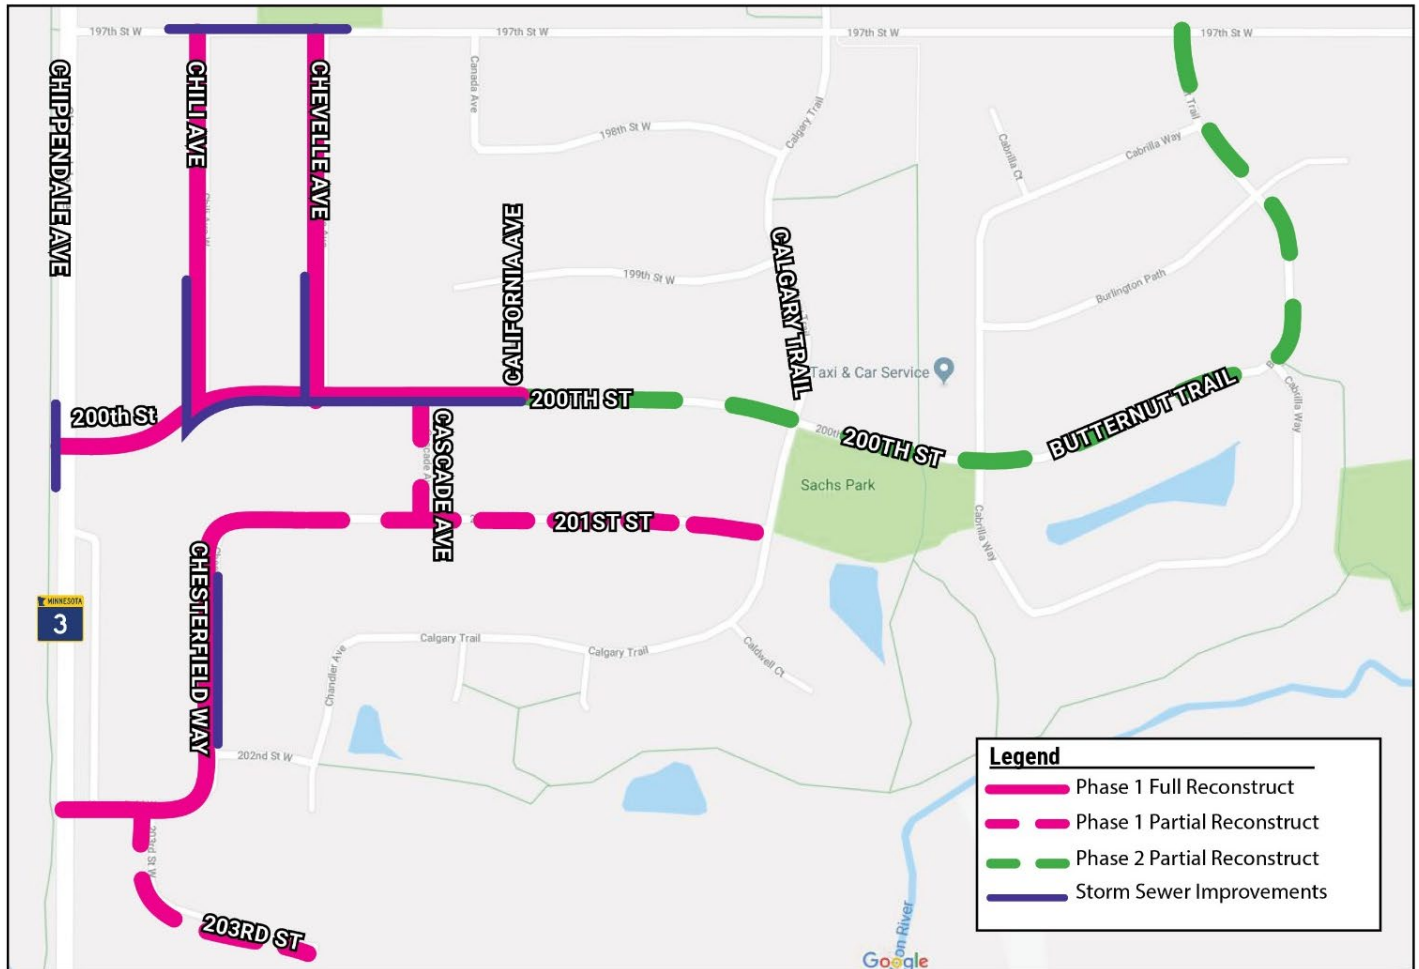

Be sure to sign up for email updates on the project website!
<http://clients.bolton-menk.com/empiretownship/2019-street-improvements-overview/>
