

2025 Street & Utility Improvement Project

Construction Newsletter

October 3rd, 2025


Schedule

2025 Start: September 8th

2025 End: Mid-November

2026 Start: April or May

2026 End: Mid-July



City of Kenyon
City Hall
709 2nd Street
Kenyon, MN 55946



**BOLTON
& MENK**

Project Engineering Firm
Bolton & Menk, Inc.

Scott Wasbotten (Primary Contact)

Construction Project Representative

Cell: 218-340-7815

Scott.wasbotten@bolton-menk.com

Derek Olinger, P.E.

Kenyon City Engineer

Cell: (507) 525-2685

derek.olerger@bolton-menk.com



Project Schedule

8th Street & 5th Street

Crews will continue to work on water and sanitary services within 8th Street during the week of October 6th. The street should be brought back to gravel during the week of October 13th.

Concrete curbing and driveways are currently expected during the week of October 20th.

Concrete needs about 1 day before you can walk on it and 1 week to drive on it. As a general rule, please do not walk on any concrete that you are seeing for the first time. This will also affect driveway access. Please plan to park on side-streets while new concrete cures.

Paving of the first layer of asphalt will occur at the end of the month.

Additional notice will be provided for paving; however, paving should only take one day and you'll be able to drive on pavement immediately after crews leave.

2nd Street Work

For the next several weeks, the contractor will be installing water lines within 2nd Street (County Rd 12). The first week of work will require 24-hour street closures. During the week of Oct 13th, closures will be limited to daytime working hours and you'll be allowed through during nights and weekends.

A separate notice has been sent out with additional detail regarding roadway closures. Pavement and sidewalk replacement is scheduled for the end of the month.

A map is provided on the next page.



Contacts

Your best source of information throughout the project will be the engineer's construction project representative, Scott Wasbotten. Reach Scott anytime at 218-340-7815 or Scott.wasbotten@bolton-menk.com.



Text or Email Updates

Sign up for text or emailed versions of construction newsletters to receive more timely information on the project. Sign up using the url below or QR code to the left



<https://clients.bolton-menk.com/kenyonstreetandutility/>

(Continued the other side)

2025 Street & Utility Improvement Project



Map

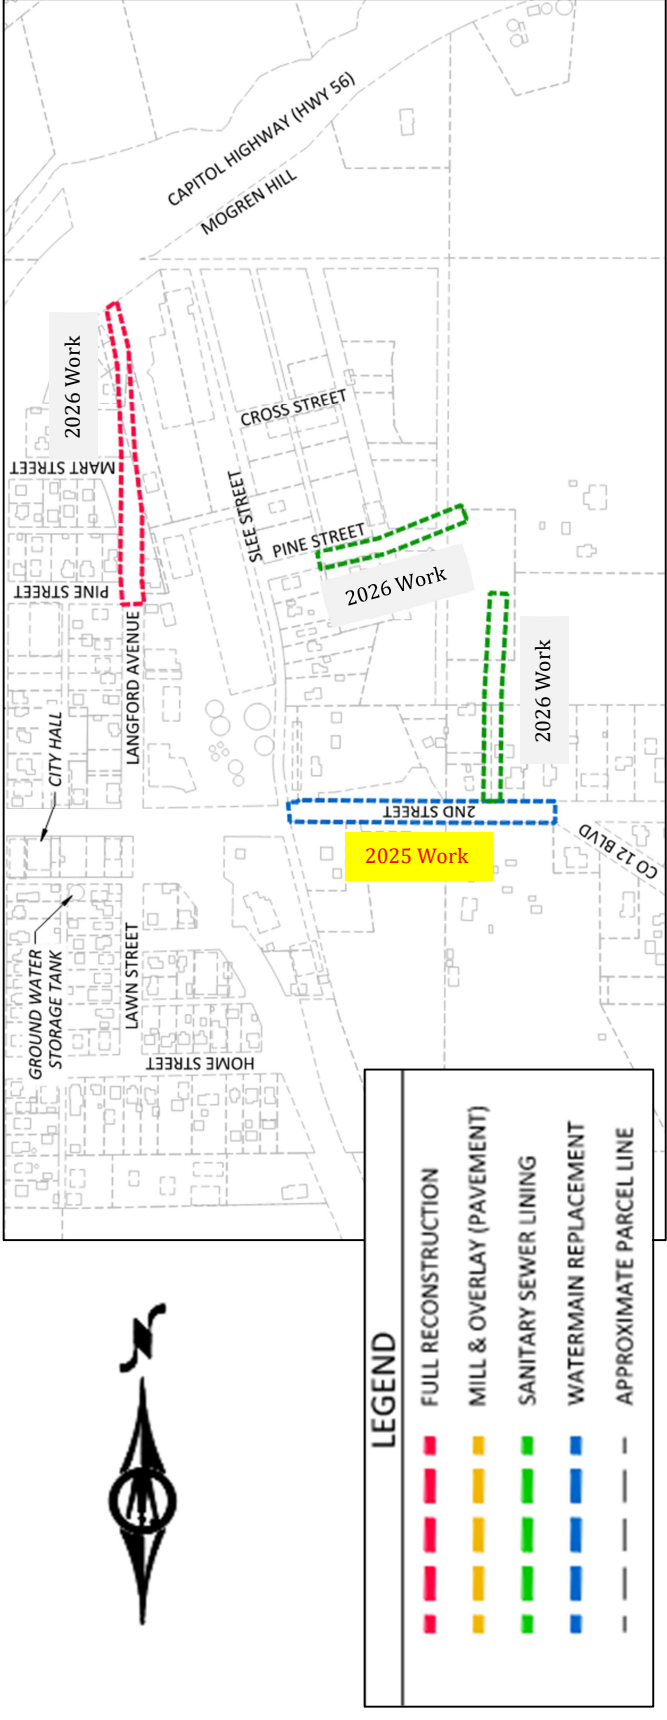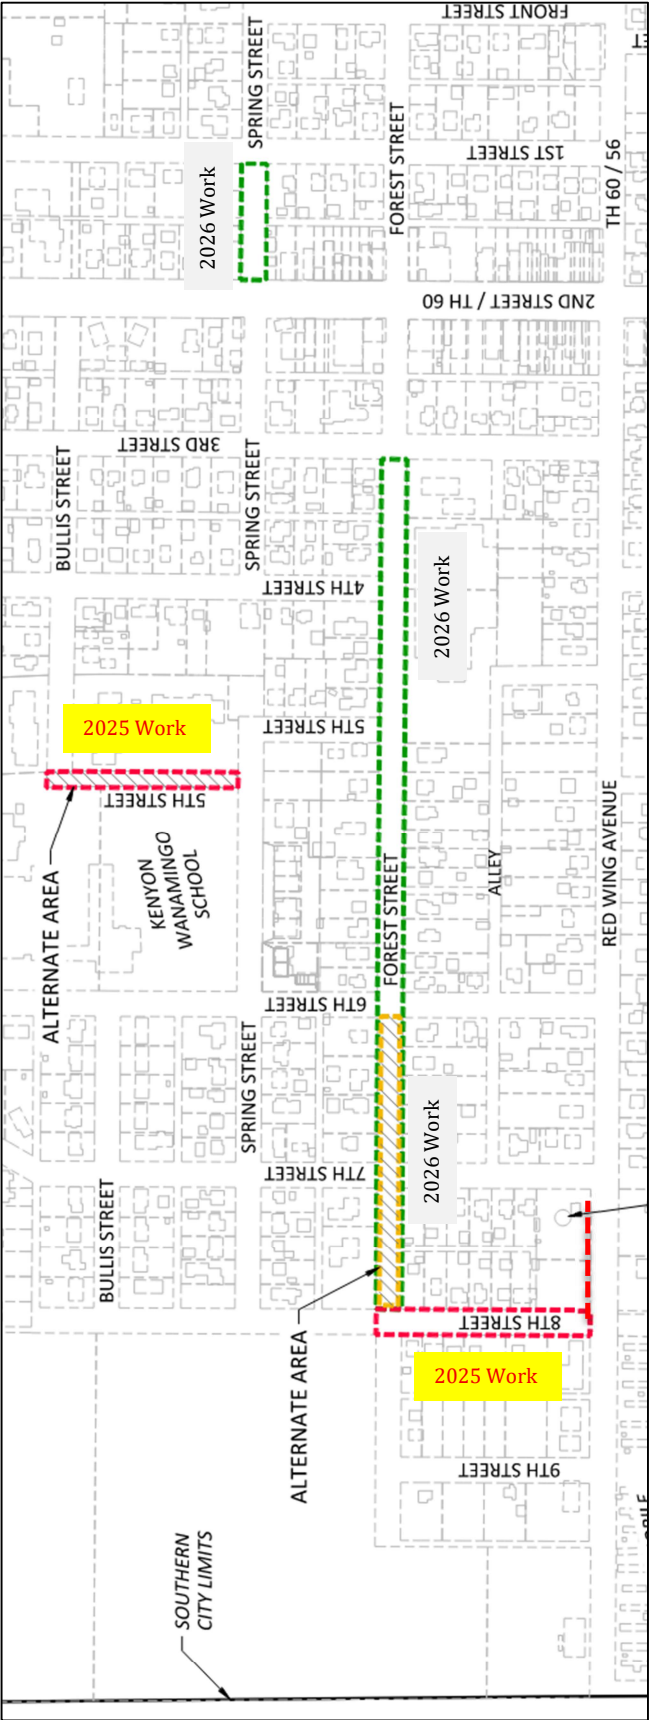

LEGEND

- FULL RECONSTRUCTION
- MILL & OVERLAY (PAVEMENT)
- SANITARY SEWER LINING
- WATERMAIN REPLACEMENT
- APPROXIMATE PARCEL LINE
