


2025-26 Street & Utility Improvement Project Construction Newsletter

June 8th, 2026

Schedule

2026 Start: April
2026 End: Mid-July



City of Kenyon
City Hall
709 2nd Street
Kenyon, MN 55946



Project Engineering Firm
Bolton & Menk, Inc.

Derek Olinger, P.E.
Kenyon City Engineer
Cell: (507) 525-2685
derek.olinger@bolton-menk.com



Project Schedule

Langford Ave

Gravel base will be placed within Langford Ave early during the week of June 8th and concrete work will start late in the week and early the week of June 15th. New curb will be placed first, followed by driveways.

Please be mindful of new concrete to avoid damage during the hardening period. You can walk on new concrete after 24 hours, but please avoid contact with any concrete you're seeing for the first time. You may drive on new concrete after about a week.

Paving is scheduled during the week of June 22nd. The last layer of pavement will be delayed until the end of summer.

Sod will be installed in July. The contractor will water grass for the first month. After this time, please begin watering and maintaining your lawn yourself. A little extra watering and keeping your mower set to its highest level (4"+) for the first year will ensure healthy growth.

8th Street

Final paving of 8th Street will be delayed till later this summer. The work is being delayed to remedy a construction issue from last year. We are also aware of a few grading issues in front yards, which should be resolved soon.

Sewer Lining (Green areas on map)

The sewer lining crews are expected to be back in town during the week of June 22nd. All areas will remain accessible during construction.

Punch List

Please contact Derek with any concerns ASAP. Repairs are more likely to occur when brought to our attention when the contractor is still in town.



Contacts

Your best source of information throughout the project will be the city engineer, Derek Olinger. Reach Derek anytime at 507-525-2685 or derek.olinger@bolton-menk.com





Project website & contacts

Please visit the project website using the URL or QR code for more information on the project.

<https://clients.bolton-menk.com/kenyonstreetandutility/>

(Continued the other side)

2025 Street & Utility Improvement Project

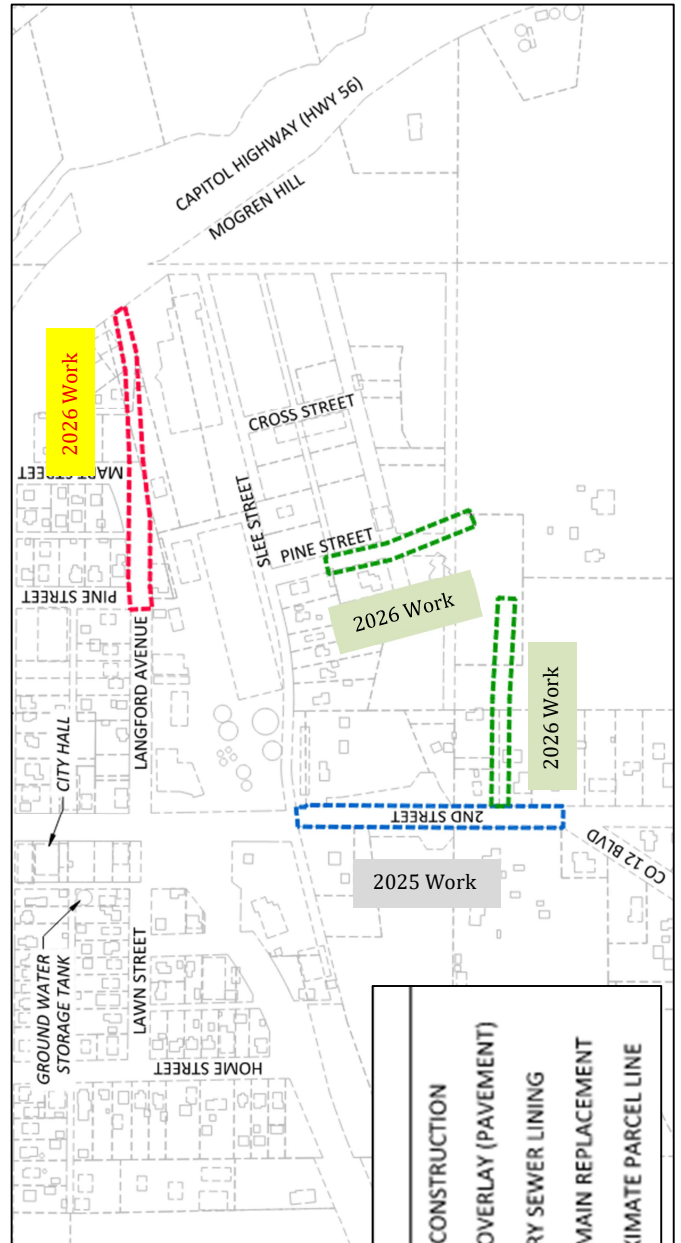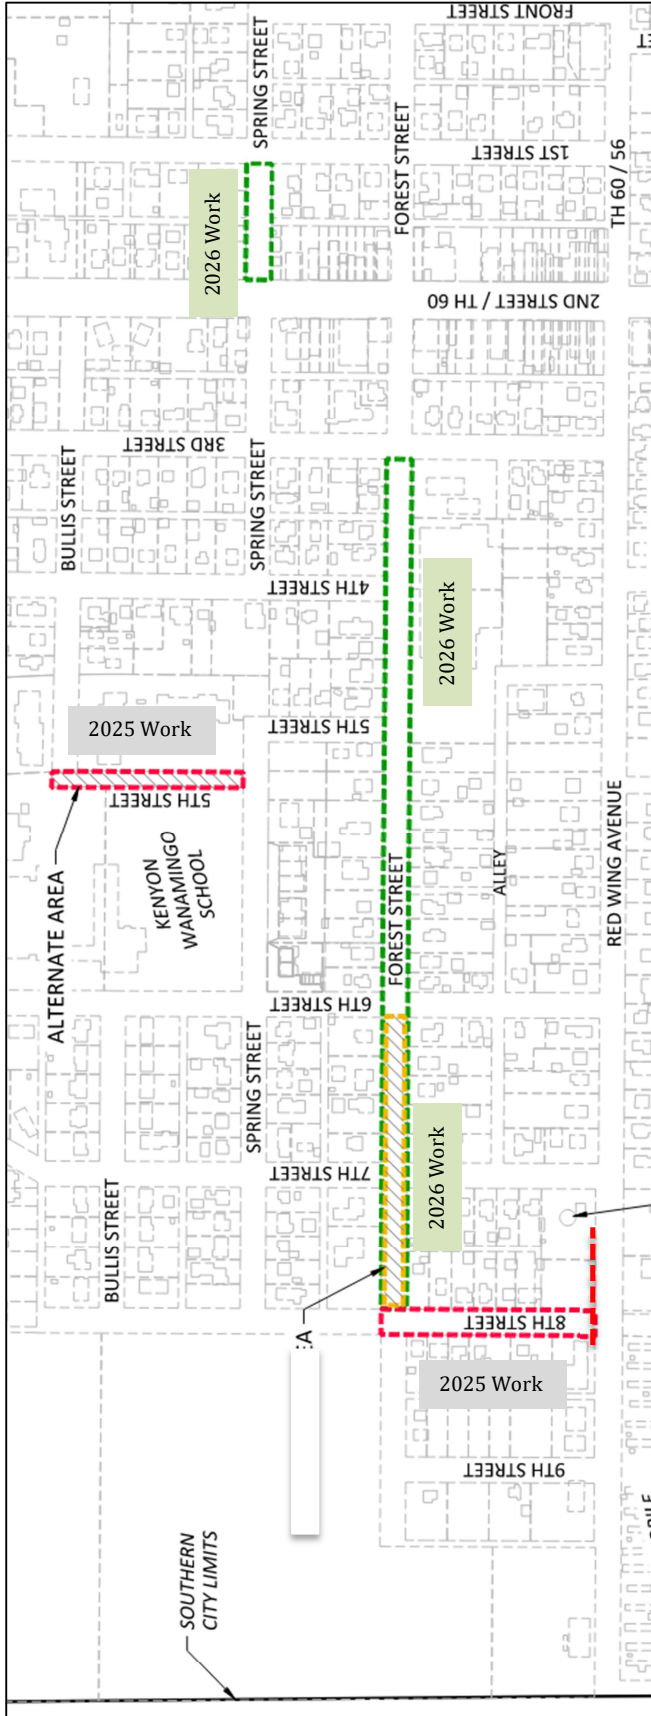

LEGEND	
	FULL RECONSTRUCTION
	MILL & OVERLAY (PAVEMENT)
	SANITARY SEWER LINING
	WATERMAIN REPLACEMENT
	APPROXIMATE PARCEL LINE
