


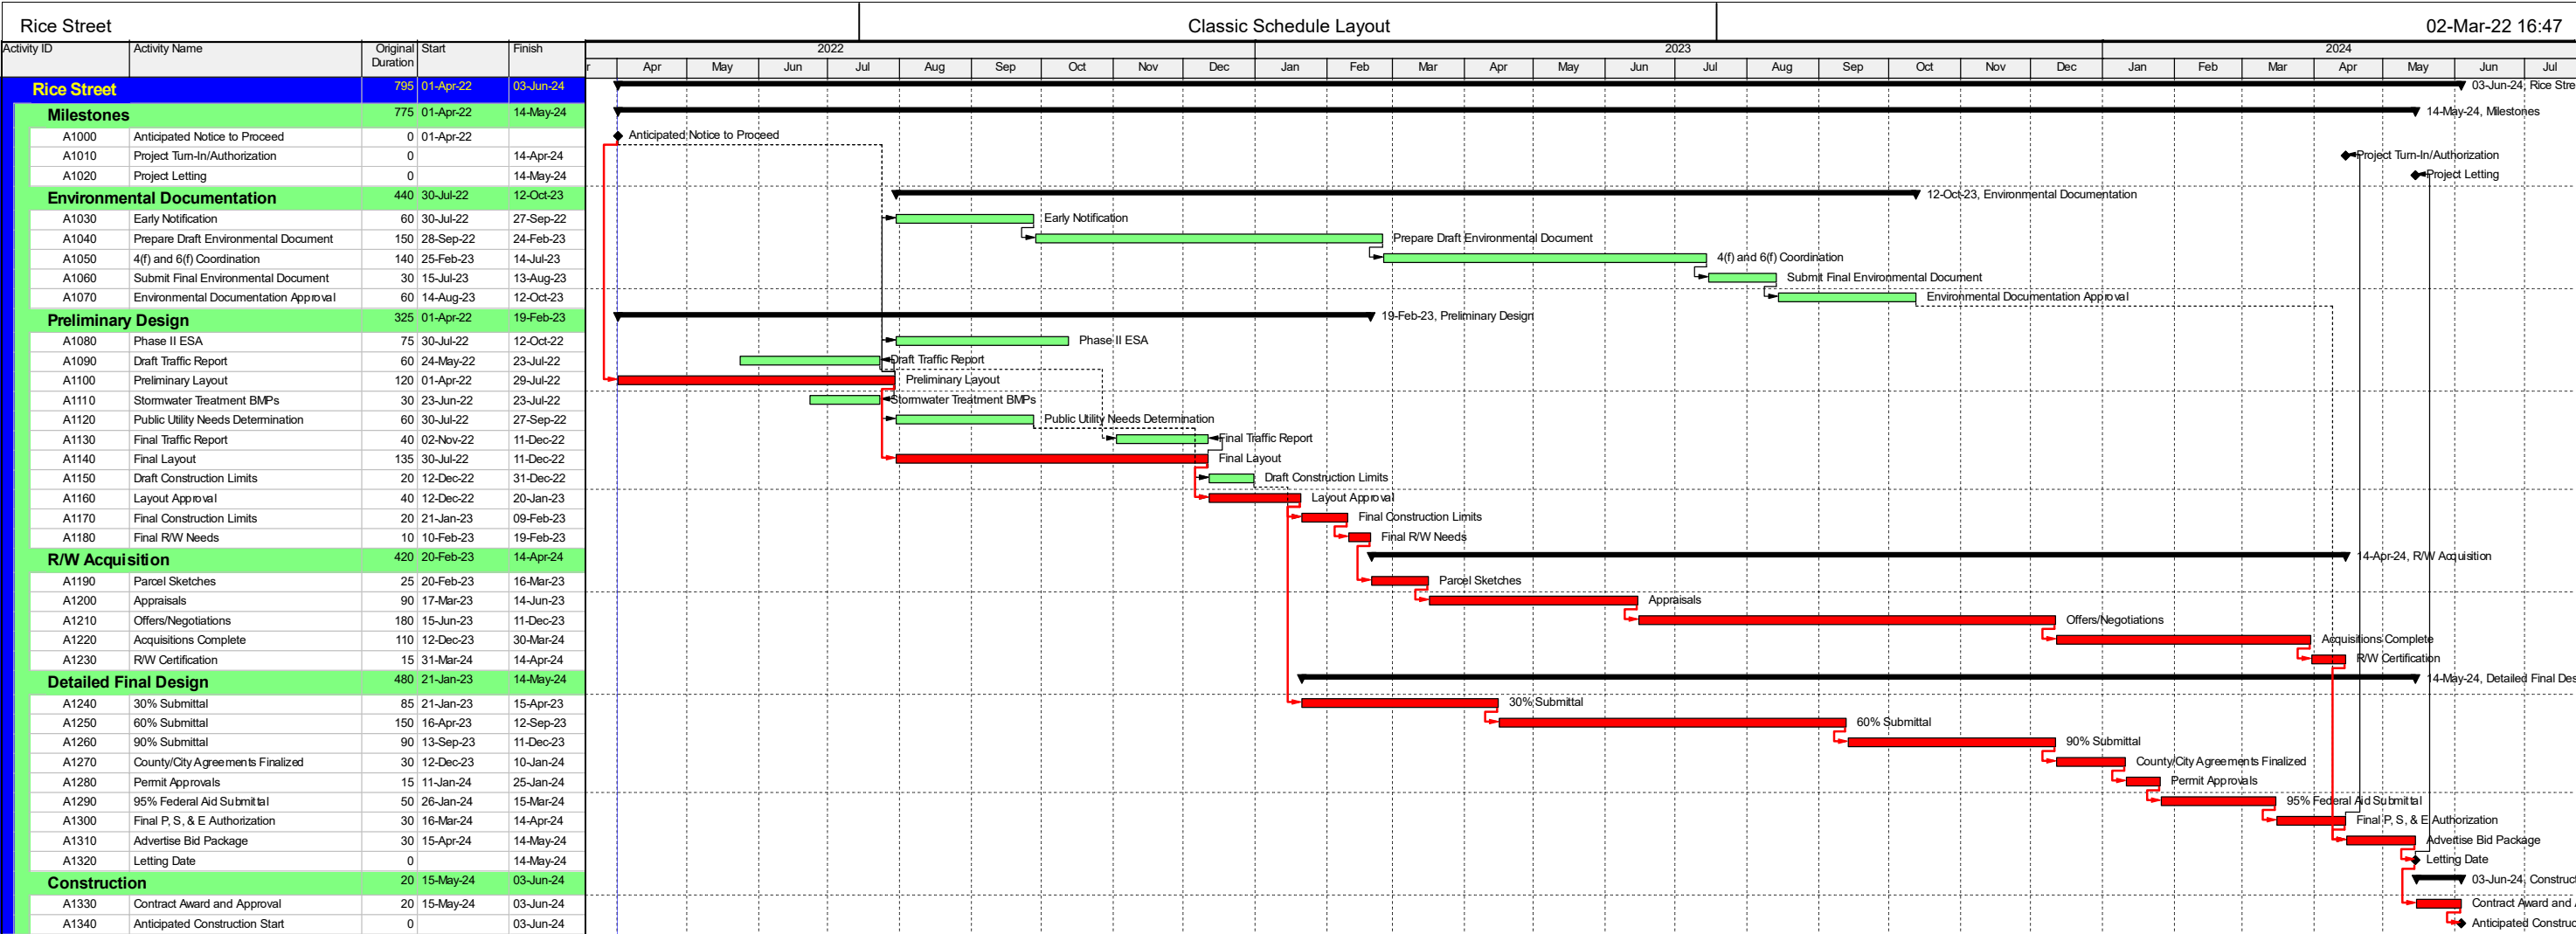

Actual Work

Critical Remaining Work

Summary


Remaining Work

Milestone

Page 1 of 1

TASK filter: All Activities

© Oracle Corporation

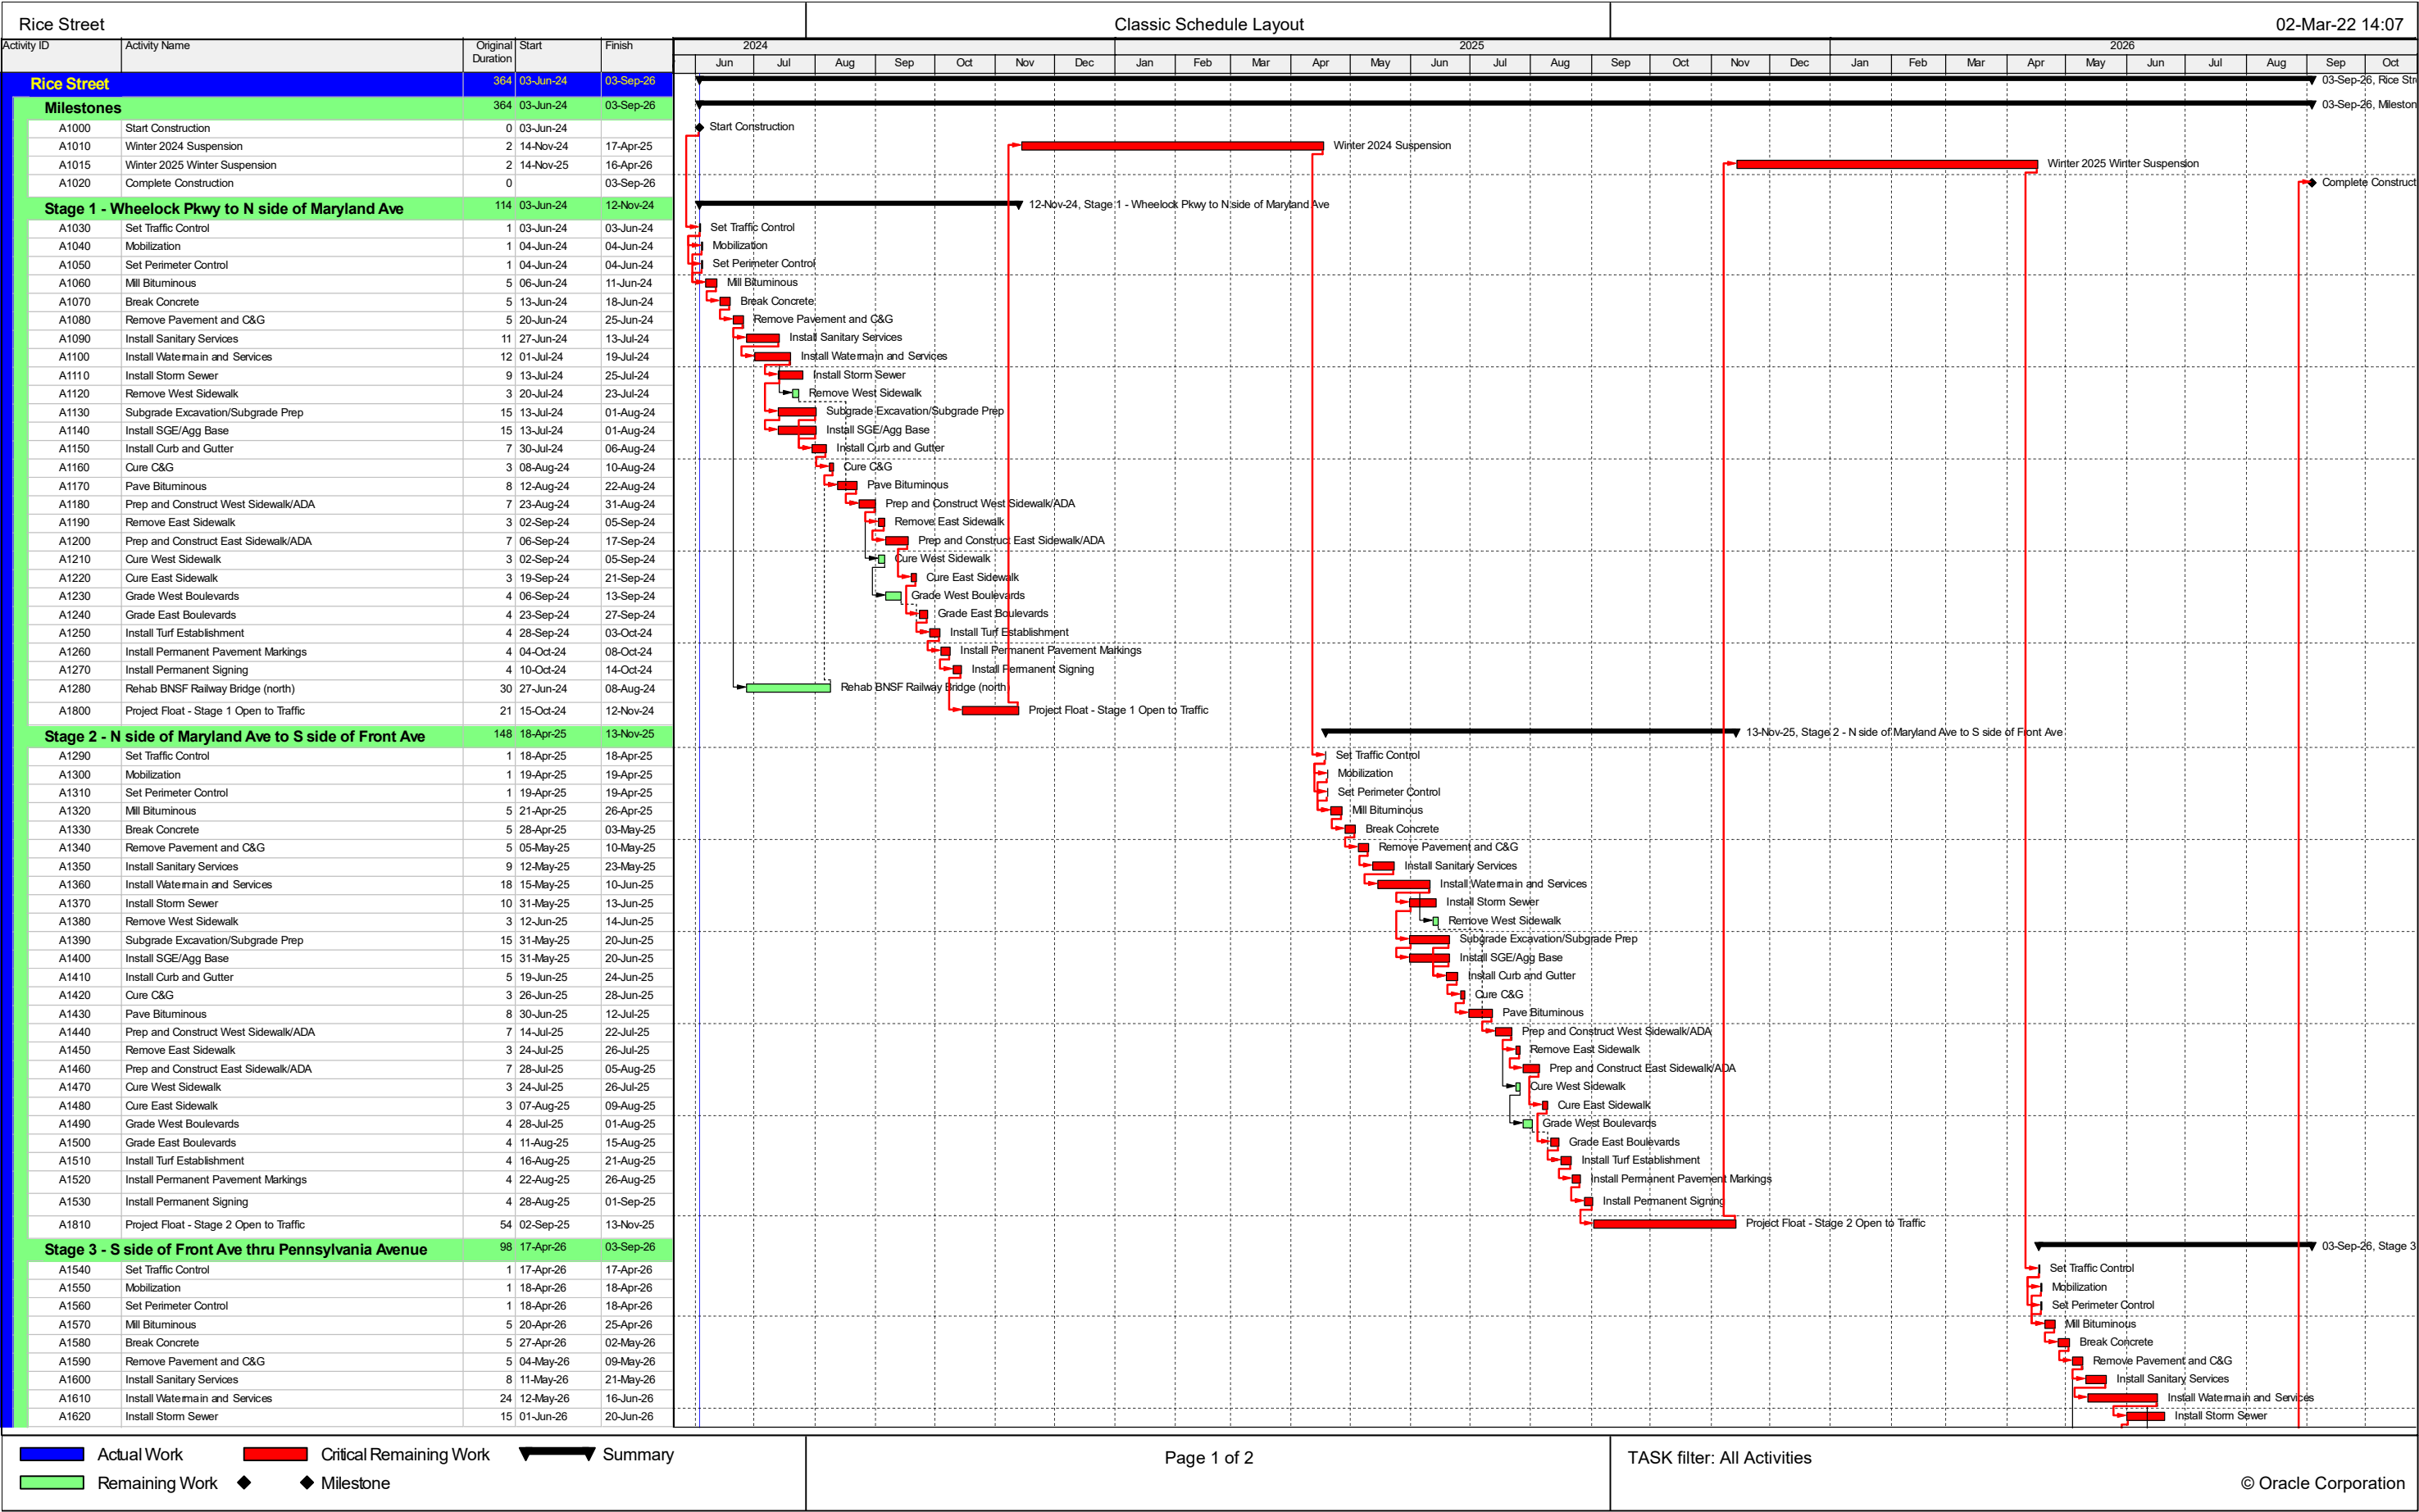

Rice Street					Classic Schedule Layout																								02-Mar-22 14:07											
Activity ID	Activity Name	Original Duration	Start	Finish	2024												2025												2026											
						Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct						
	A1630	Remove West Sidewalk	3	18-Jun-26	20-Jun-26																																			
	A1640	Subgrade Excavation/Subgrade Prep	15	05-Jun-26	25-Jun-26																																			
	A1650	Install SGE/Agg Base	15	05-Jun-26	25-Jun-26																																			
	A1660	Install Curb and Gutter	6	22-Jun-26	29-Jun-26																																			
	A1670	Cure C&G	3	30-Jun-26	03-Jul-26																																			
	A1680	Pave Bituminous	8	04-Jul-26	14-Jul-26																																			
	A1690	Prep and Construct West Sidewalk/ADA	7	16-Jul-26	24-Jul-26																																			
	A1700	Remove East Sidewalk	3	25-Jul-26	28-Jul-26																																			
	A1710	Prep and Construct East Sidewalk/ADA	7	30-Jul-26	07-Aug-26																																			
	A1720	Cure West Sidewalk	3	25-Jul-26	28-Jul-26																																			
	A1730	Cure East Sidewalk	3	08-Aug-26	11-Aug-26																																			
	A1740	Grade West Boulevards	4	30-Jul-26	03-Aug-26																																			
	A1750	Grade East Boulevards	4	13-Aug-26	17-Aug-26																																			
	A1760	Install Turf Establishment	4	18-Aug-26	22-Aug-26																																			
	A1770	Install Permanent Pavement Markings	4	24-Aug-26	28-Aug-26																																			
	A1780	Install Permanent Signing	4	29-Aug-26	03-Sep-26																																			
	A1790	Rehab BNSF Railway Bridge (south)	30	11-May-26	23-Jun-26																																			

