

## Project Update—February 28, 2019

### Week of February 25

Crews continued box culvert installation near Red Lobster.

### Week of March 4

Crews will finish up box culvert construction near Red Lobster. Crews will then begin installing storm sewer south of Morgan Circle.

Beginning March 11, work will begin on the east half of Morgan Circle. This work includes installing new sanitary and storm sewer, curb, and pavement. The east half of Morgan Circle will be closed during this work, which will take about a month. The west side of Morgan Circle will remain open during this work, but using alternate routes will be easier to access businesses (see access map on page two).



*Box culvert installation*

# BLOOMINGTON Penn American




www.BloomingtonPennAmerican.com

## BLOOMINGTON PENN AMERICAN MORGAN CIRCLE ACCESS PLAN

ENTRY ROUTE

EXIT ROUTE

CONSTRUCTION AREA

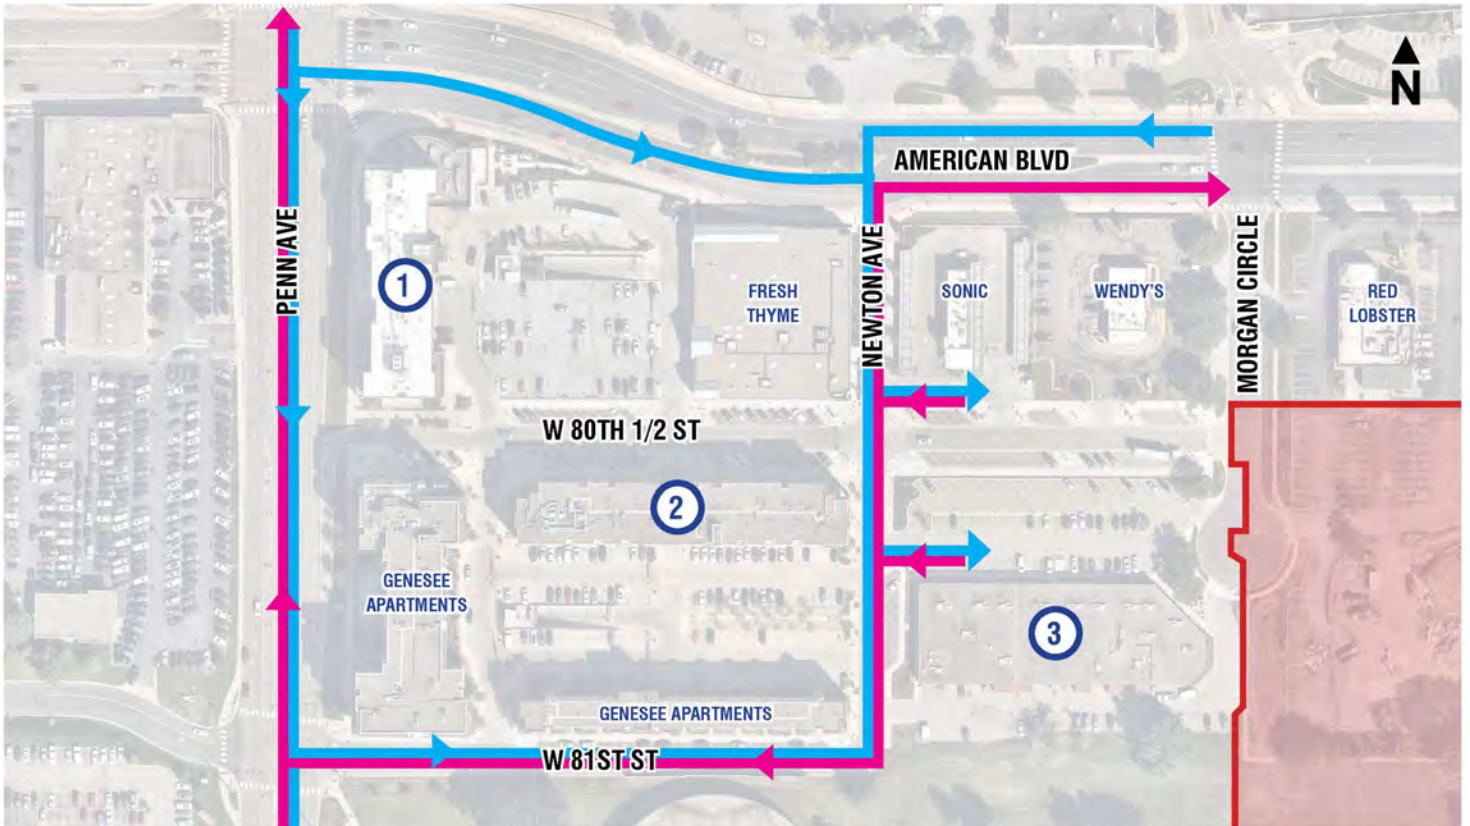

**1** AT&T  
Red Robin  
Home2 Suites by Hilton

**2** Moe's Southwest Grill  
Fantastic Sams  
Krengel Dental  
Bloomington Eye Center

Which Wich  
CPR Cell Phone Repair

**3** The Yoga Pioneers  
Bharat Bazaar  
Tandoor  
Liquor Locker

Hunan  
Best Friends Animal Hospital  
The Fringe Salon

