



# 2019 Street Improvements Project Update

July 1, 2019

*Please view the phasing map on page two.*

## Week of June 24

- Storm sewer installation was completed on Chili and Chevelle.
- Storm sewer installation began on Chesterfield.
- Gate valve replacement work on 200th Street and on Butternut Trail was completed.
- Sanitary manhole work was completed.
- Reclaiming of the pavement into a driveable gravel surface was completed on the Phase 1 and Phase 2 Partial Reconstruct areas.

## Week of July 1

- The contractor does not plan on working July 4-7. They will be returning to the site on July 8.
- Storm sewer installation will be completed on 200th Street and on Chesterfield Way.
- **On Tuesday, July 2, the contractor will be closing access to 200th Street at Highway 3** to complete a culvert installation. Please plan to use 197th Street or Chesterfield Way to access/exit Highway 3 on this day. 200th Street will be open east of Chili Avenue during this time. Access to Highway 3 from 200th Street will be reopened at the end of the work day (7 PM).
- The contractor plans to mill the top 4 inches of gravel off the streets that are part of the Phase 1 and Phase 2 Partial Reconstruct areas. A ramp will be provided to driveways for residents living on these streets.
- Paving of the Phase 1 and Phase 2 Partial Reconstruct areas is planned for the week of July 8.

## Parking, access, and detour information

During construction, the contractor will typically work from 7 a.m. to 7 p.m. On-street parking will not be available during working hours. If you need to leave past 7 a.m., you may need to park on another nearby street. Access to driveways will be restored at the end of each work day. If you have a recreational vehicle that you need a place to park during the concrete work the Township has approved parking in the Town Hall Parking Lot off of 197th Street.

## Contacts

If you have any questions or concerns, please contact **Eric Hauser at (507) 276-6695**.



**Be sure to sign up for email updates on the project website!**


<http://clients.bolton-menk.com/empiretownship/2019-street-improvements-overview/>





# 2019 Street Improvements Project Update

## Phasing Map

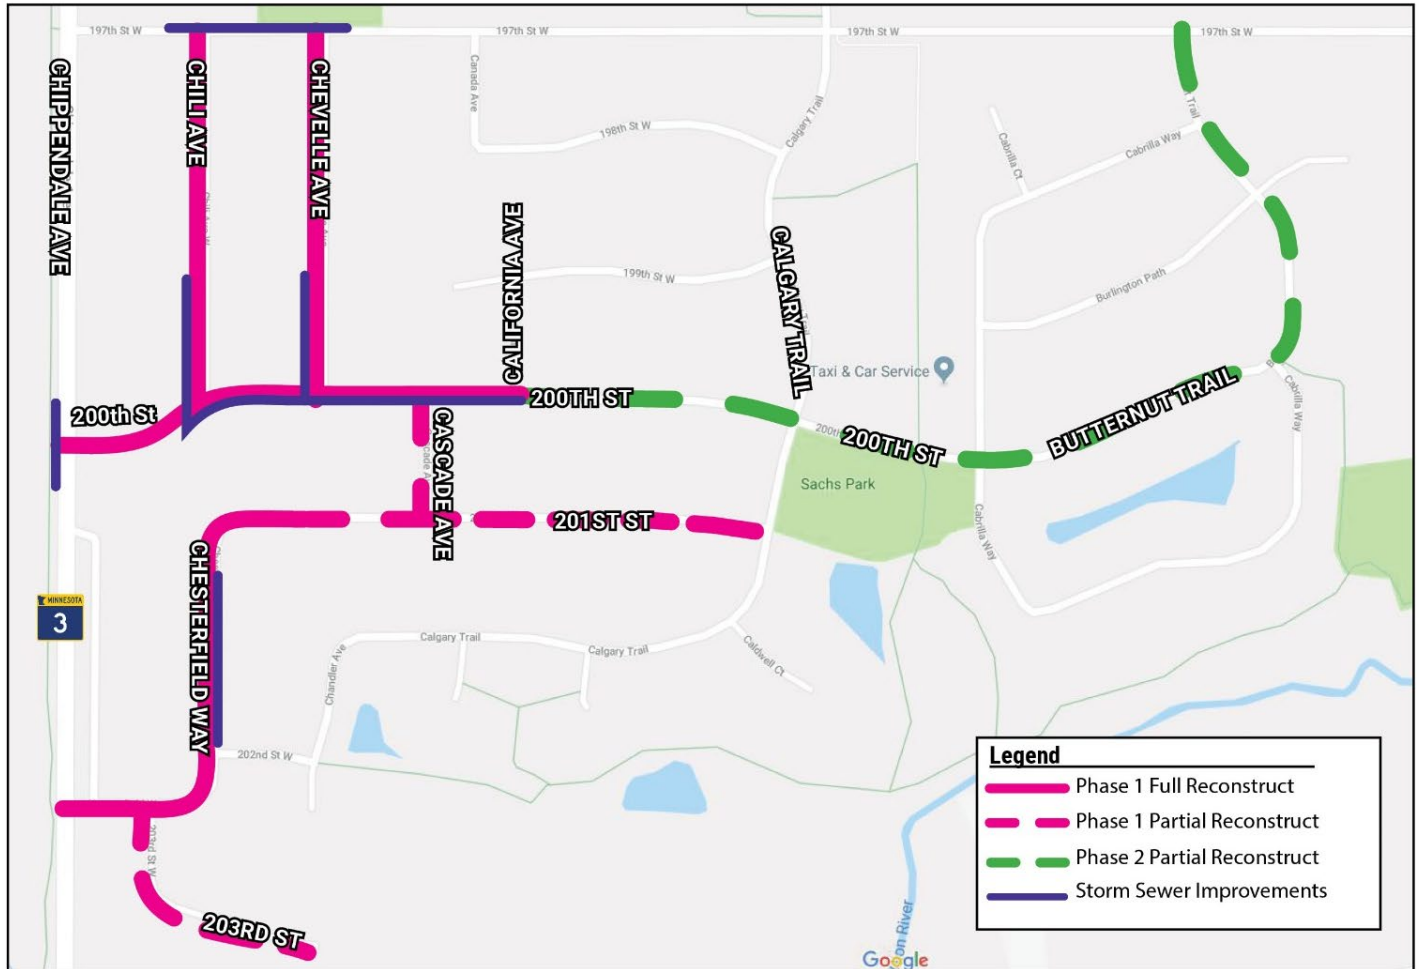

Be sure to sign up for email updates on the project website!  
<http://clients.bolton-menk.com/empiretownship/2019-street-improvements-overview/>

