



2019 Street Improvements Project Update

August 5, 2019

Please view the phasing map on page two.

Week of July 29

- The Phase 1 Full Reconstruct areas were graded and paved.
- Boulevards in the Phase 1 Full Reconstruct areas were graded. Crews started bringing in top soil to place in the boulevards.
- Crews started paving driveways in the Phase 1 Full Reconstruct areas.

Week of August 5

- Driveway work will be completed.
- Sod will be placed throughout the Phase 1 and Phase 2 areas. The contractor is responsible for maintaining the sod for a period of 30 calendar days from installation. Although the contractor is responsible for maintaining the sod, they would greatly appreciate any assistance you can give them by watering the sod to help with establishment.
- As mentioned in the newsletters, any damage to private features (such as irrigation) within the Township right of way will not be repaired, replaced, or altered by the Township or the contractor. It is recommended that any irrigation repairs be scheduled shortly after the top soil has been installed. The top soil should be installed by the middle of the week.

Parking, access, and detour information

During construction, the contractor will typically work from 7 a.m. to 7 p.m. On-street parking will not be available during working hours. If you need to leave past 7 a.m., you may need to park on another nearby street. Access to driveways will be restored at the end of each work day.

Contacts

If you have any questions or concerns regarding this update or the project in general, please contact **Eric Hauser at (507) 276-6695**.



Be sure to sign up for email updates on the project website!


<http://clients.bolton-menk.com/empiretownship/2019-street-improvements-overview/>





2019 Street Improvements Project Update

Phasing Map

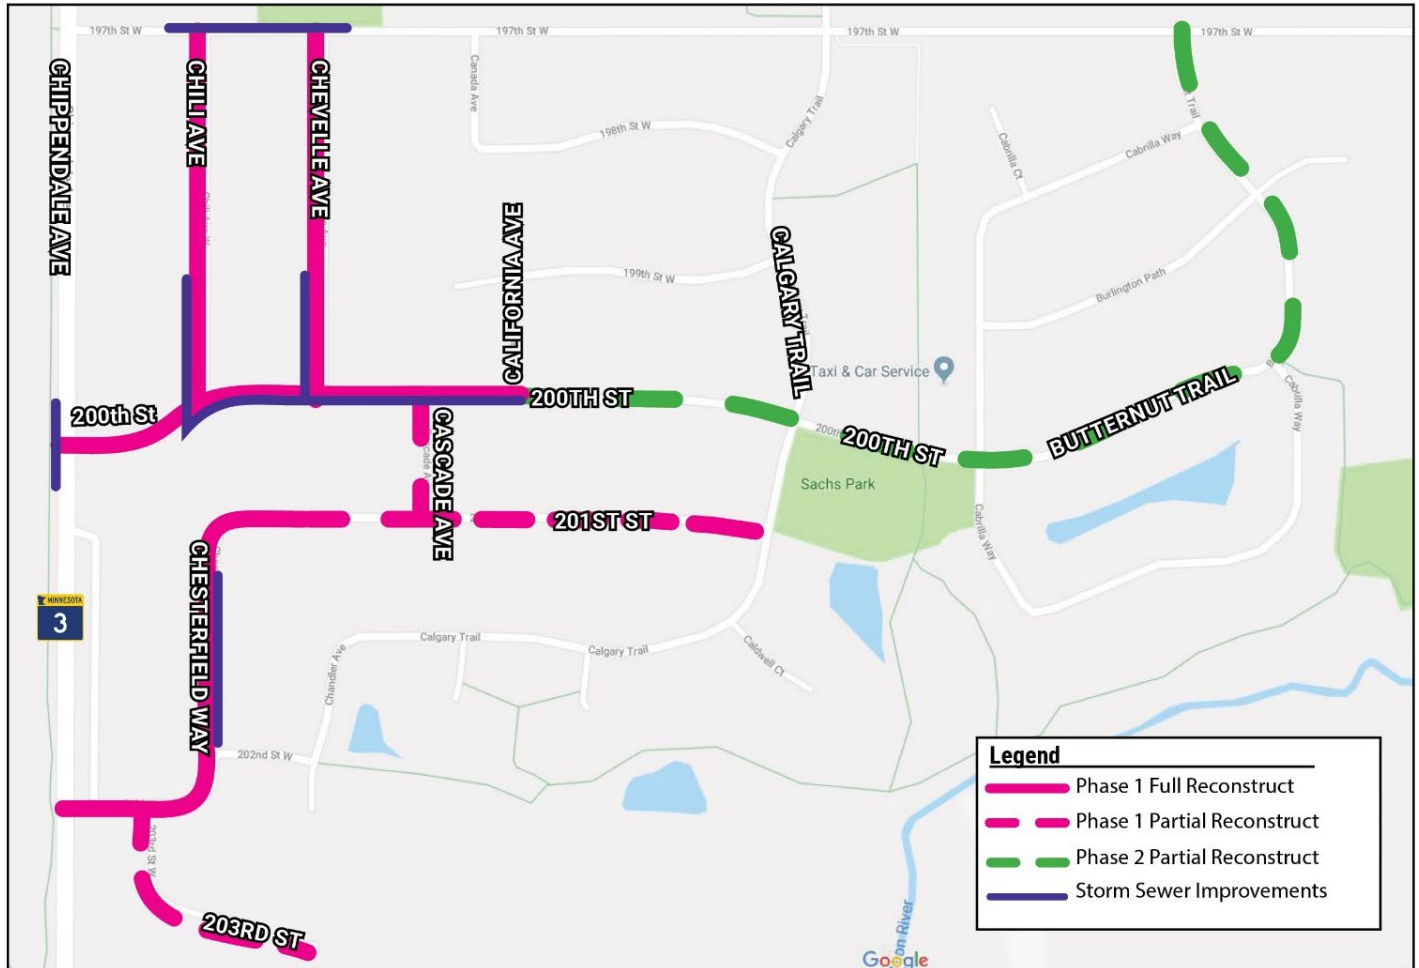

Be sure to sign up for email updates on the project website!

<http://clients.bolton-menk.com/empiretownship/2019-street-improvements-overview/>

