

Sunset Drive Improvement Project

City of Jordan and Jordan Independent School District 717



Construction Newsletter 02 - July 2025

OVERVIEW

Construction of the Sunset Drive Improvements along Sunset Drive and Hillside Drive nearby the Jordan Schools' campuses is ongoing. The project involves the addition of two roundabouts and pedestrian crossing improvements to increase safety and efficiency for traffic and pedestrians. The project layout can be found on the other side of this page.

Reminder: Sunset Drive and Hillside Drive from Aberdeen Avenue to just west of Cedar Lane is closed to traffic. Please refer to the map on the other side of this newsletter for the closure limits and alternative routes to avoid the closure area. Please note that anyone seen moving construction traffic control or driving through the project area may be ticketed by police. Thank you for your cooperation and patience during the construction of these improvements!

PROJECT UPDATES/SCHEDULE

- Public utility construction (watermain, sanitary sewer, and storm sewer) is underway and expected to be completed by early July.
- Roadway grading for the western roundabout at the new entrance to the elementary school and entrance to the CERC is completed. Concrete curb and gutter will be installed in mid-July.
- Roadway grading of the eastern roundabout near the Sunset Drive / Hillside Drive / High School entrance intersection will be completed in early to mid-July. Concrete curb and gutter is estimated to be completed in late-July.
- Concrete median/sidewalk construction, bituminous/asphalt trail paving, roadway paving, enhanced pedestrian crossing construction, lighting, and boulevard restoration will be completed in August.
- The project is estimated to be substantially completed and opened to motorists by the end of August.
- Final project cleanup will be completed during the fall of 2025.

CONSTRUCTION ZONE SAFETY

Some residents (especially children) may become curious about the work the Contractor is performing. Please stay clear of construction zones when possible. Hazards inherently exist around heavy machinery, trenches, unstable material, confined buried spaces, hot asphalt, etc. and may not be easily recognizable by all. The Contractor will promote safety within the construction area, though everyone should also take personal measures to remain safe during construction. Any direction from the Contractor regarding safety must be followed, including signage or direction given by contractor field staff. If you observe an unsafe condition, please report it to the project hotline at (952)-698-0378.

Contacts

Project Phone Hotline:

- (952)-698-0378

Alex Madson

On-site Construction Manager
Bolton & Menk

- (952) 256-3222
- Alex.Madson@bolton-menk.com

Project Website



Scan the QR code or visit jordanmnengineering.com to learn more and sign up for email or text updates!


Sunset Drive Improvement Project

City of Jordan and Jordan Independent School District 717



Construction Newsletter 02 - July 2025

CLOSURE, DETOUR AND ACCESS MAP

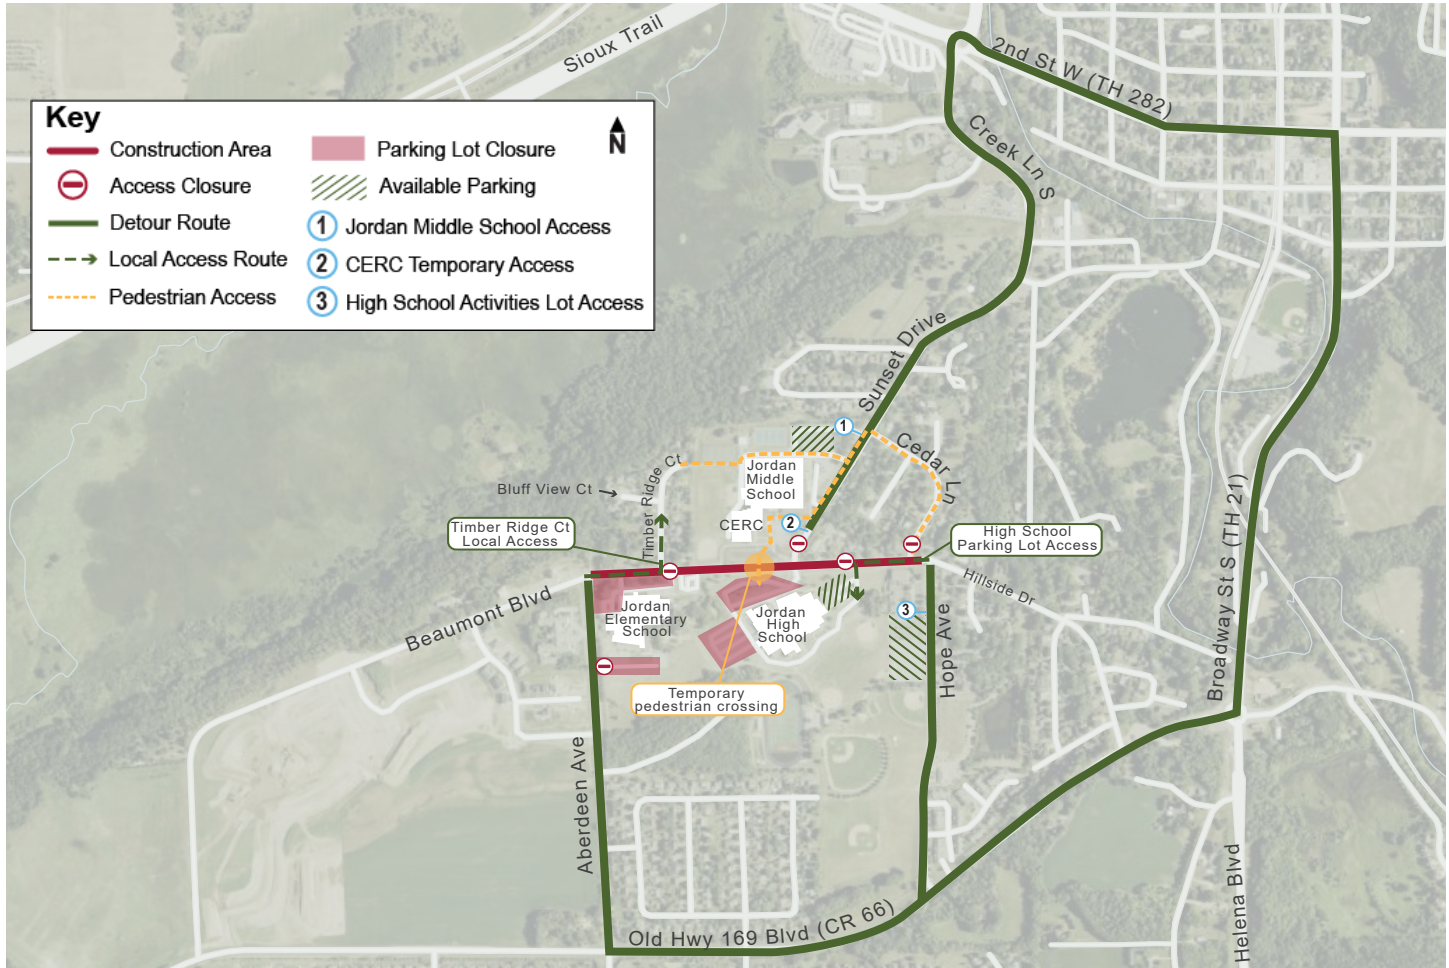

PROJECT LAYOUT

