

This project is intended to begin the transformation of the Broadway Avenue corridor (from Civic Center Drive to 13th Street North) into a significant multi-modal gateway to downtown Rochester and the Destination Medical Center (DMC) Development District.

CONSTRUCTION UPDATE

As we head into fall, the construction continues to progress at the south end of the project. The 13th Street intersection has been established as a three-way stop for a few weeks and will operate as-is until traffic is open on Broadway down to 7th Street. The full corridor is expected to open on November 19th.

The pavers, which will be laid between the sidewalk, and the cycle track have had a supply issue; they are expected to be in the week of October 11th. Once those are in, the area from 13th to 7th Street is ready for installation.

Elton Hills Bridge Construction

The Elton Hills Bridge construction will start on October 11th with a full closure of Elton Hills Drive over the Zumbro river. Traffic will detour south from Elton Hills Drive NW down to 13th Street NW, and then north on Broadway. Construction is expected to be complete by Summer of 2022.

11th Street to 7th Street


The road and sidewalk are complete, and concrete will be finished for the cycle track by October 11th. Pedestrians can currently use the sidewalk on both sides.

7th Street to Civic Center

Utility work continues in this area, and the concrete will be poured on Broadway the week of 10/18. The pedestrian path is currently on the west side down to 5th Street, and then detouring around the Bryk on Broadway site to Civic Center Drive

**All dates are weather-dependent.*

These travel impacts are related to the [North Broadway Reconstruction Project](#).

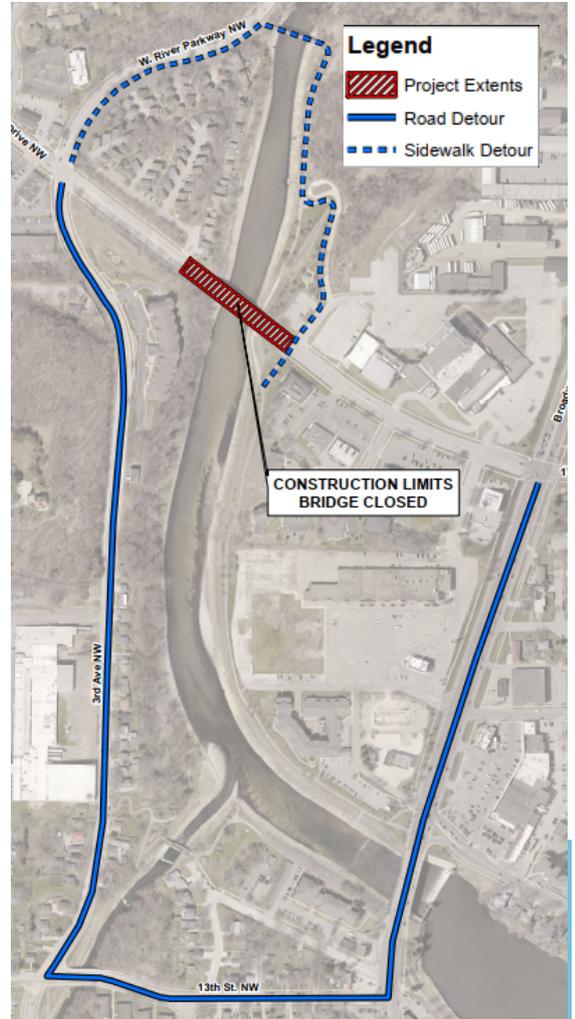

Detour map for Elton Hills Bridge construction starting October 11

PROJECT CONTACTS

- CORY PENZ, ELCOR PROJECT ACCESS MANAGER**
507-735-0150 •
CORY@ELCORCONSTRUCTION.COM
- MATT SMITH, ELCOR PROJECT MANAGER**
507-951-1062 •
MATT@ELCORCONSTRUCTION.COM
- JAYMI WILSON, COMMUNITY LIAISON PROJECT MANAGER**
507-328-2023 •
JWILSON@ROCHESTERMN.GOV
- JOSH FJETLAND, PROJECT INSPECTOR**
507-269-2223 •
JFJETLAND@ROCHESTERMN.GOV

PLEASE JOIN!

The next stakeholder meeting on October 20th will include further details on reopening the main Broadway corridor. The link for the meeting can be found on the [Get Involved Tab](#).
