

NORTH BROADWAY

This project is intended to begin the transformation of the Broadway Avenue corridor (from Civic Center Drive to 13th Street North) into a significant multi-modal gateway to downtown Rochester and the Destination Medical Center (DMC) Development District.

CONSTRUCTION UPDATE

Construction is progressing and the project is currently in position to meet the expected completion timeline of September 2022.

Project Updates:

- Utility work is nearly complete.
- Crews have started installing trees and other plantings
- Concrete work including curb & gutter continues on the west side streets, with the first lift of bituminous paving to follow
- Final lifts of pavement on the east side streets are in progress
- The areas immediately adjacent to the Benaiah project on 8th Street NE and the Bryk on Broadway project on 5th Street NW will lag behind progress in other areas, but we hope to be fully reconstructed in all areas before winter

**All dates are weather-dependent.*

PROJECT CONTACTS


CORY PENZ, ELCOR PROJECT ACCESS MANAGER
507-735-0150 • CORY@ELCORCONSTRUCTION.COM

MATT SMITH, ELCOR PROJECT MANAGER
507-951-1062 • MATT@ELCORCONSTRUCTION.COM

**JAYMI WILSON, COMMUNITY LIAISON
PROJECT MANAGER**
507-328-2023 • JWILSON@ROCHESTERMN.GOV

PAUL GRAFF, PROJECT INSPECTOR
507-254-7153 • PGRAFF@ROCHESTERMN.GOV

IMPACTS AS OF AUGUST 4:

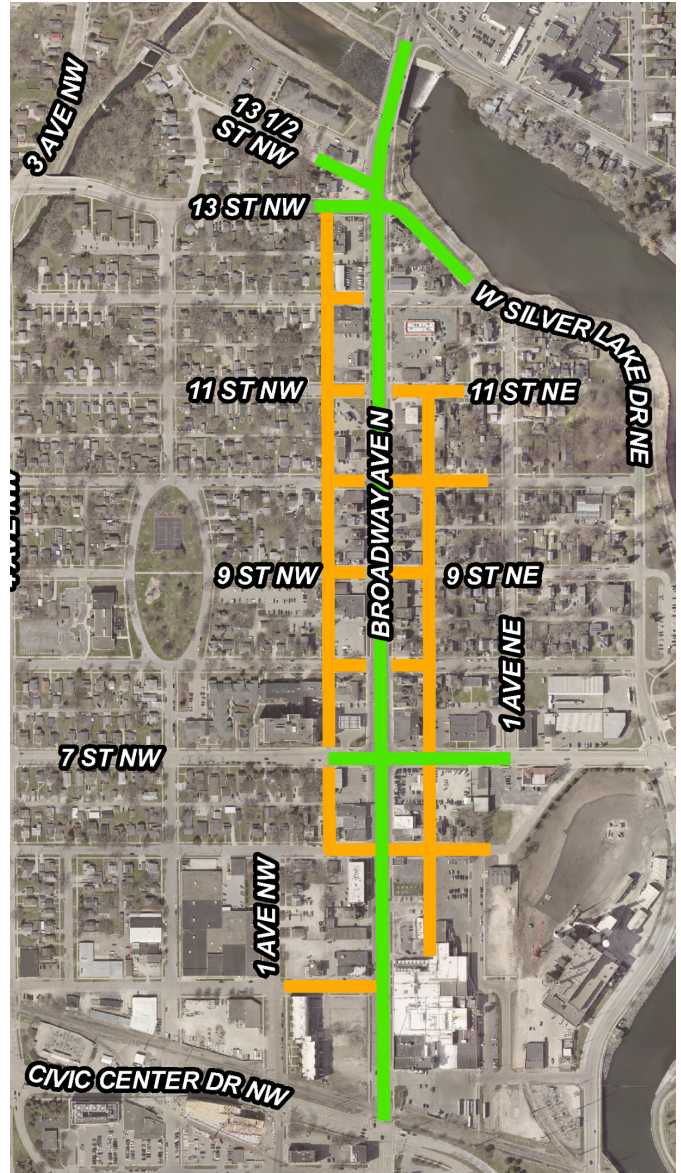

- Open with minimal impacts
- Street and sidewalk reconstruction - impacts and timing will vary

PLEASE JOIN!

Stakeholder meetings will be held the first and third Wednesday of each month. The link for the meeting can be found on the "[Get Involved](#)" tab on the website.
