



# PROJECT UPDATE

May 18, 2018

## Phase 1 (see staging map on page 2)

### Stage 1 and Stage 2 (May –End of July)

#### Week of May 14 Recap

- Construction began on Monday, May 14. This is in exception to 12th Ave to 14th Ave, which will begin at a later date.
- Milling, which involved grinding up the top couple inches of the road, occurred from 20th Ave to 14th Ave
- Temporary fences installed
- Temporary water installation began
- Reclaiming is scheduled to begin Friday, May 18.

#### Week of May 21 Activity

- Watermain and hydrant work at the 20th ave intersection
- Concrete curb, sidewalk, and driveway removals from 20th Ave to 14th Ave
- Continue temporary water began from 20th Ave to 15th Ave
- Watermain installation will begin at 20th Ave working eastward

## Southview Center Parking Lot Reconstruction

### Phase 1

#### Week of May 14 Recap

- Pavement was marked
- Milling occurred

#### Week of May 21 Activity


- Curb and gutter will be removed

### Parking and Access Information

During this time, the roadway will be closed to thru traffic but will remain open for residents and businesses to access their driveways. All north-south dead end intersections will also be maintained so residents and businesses may access their driveways. Access to individual driveways may be unavailable at times during working hours, but access will be restored each night. Traffic and transit stops will be detoured to Marie Ave during this time. The project contractor (Park Construction) will typically be working 7 a.m. to 7 p.m. Monday through Friday, with some Saturday work.

*Thank you for your patience throughout this process! Be sure to sign up for email updates at the project website. If you have any concerns, please contact the project hotline listed below.*

# Stage 1 Staging Map

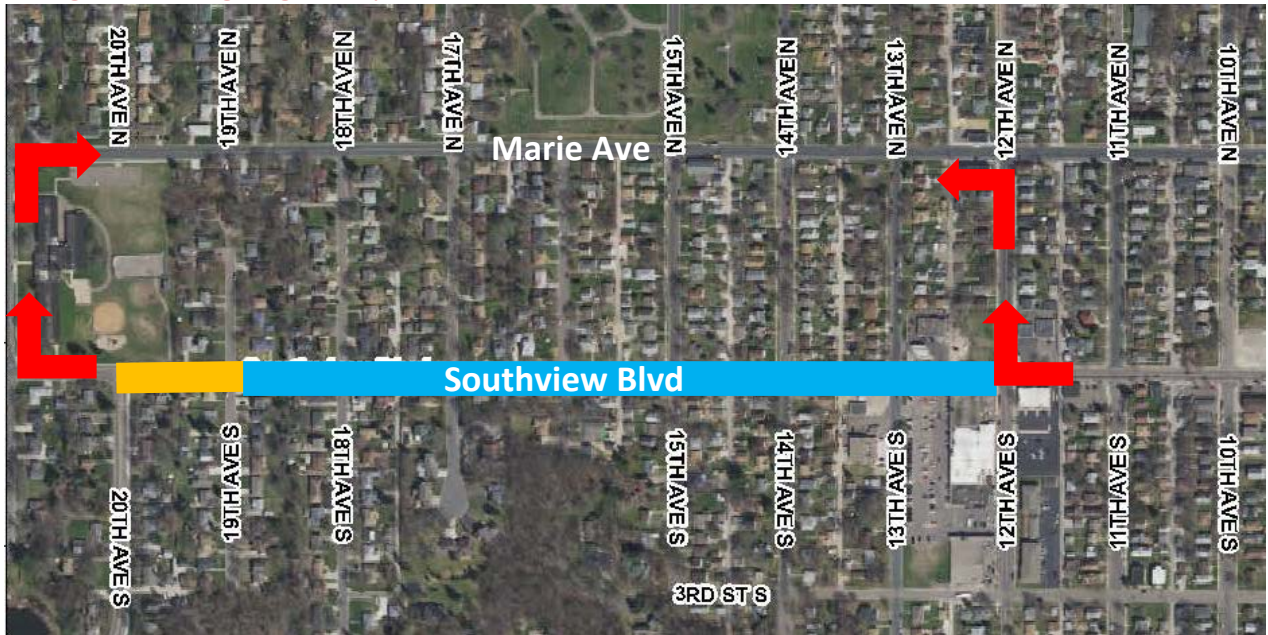

Phase 1, Stage 1		Detour Route	
Phase 1, Stage 2			

Project Hotline: 612-619-6284  
Project Website: [www.southviewblvd.com](http://www.southviewblvd.com)
